Designate location of all lateral arms and longitudinal stabilizing devices on the blocking plan.

Lateral Arm



Longitudinal Stabilizing Devices

Blocking Plan

typical single wide blocking plan

Manufacturer _____
Length x width _____

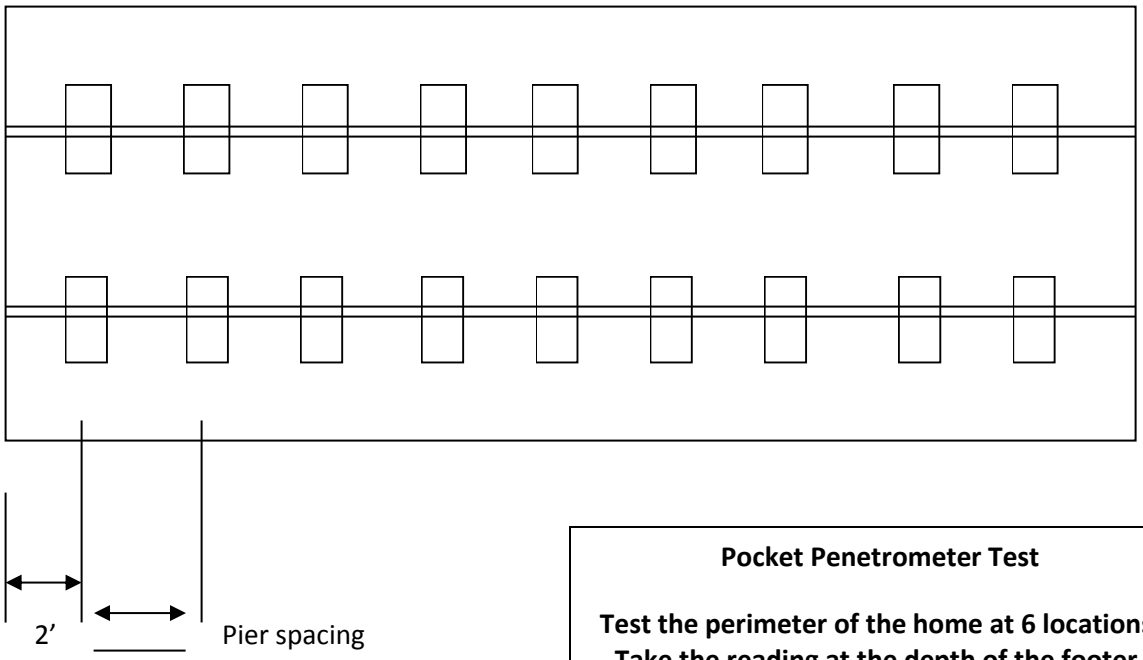

Pocket Penetrometer Test

Test the perimeter of the home at 6 locations. Take the reading at the depth of the footer. Using 500lb increments, take the lowest reading and round down to that increment.

Pocket Penetrometer test results _____
Soil torque probe test results _____
Anchor Length _____
I-beam pier pad size _____
Perimeter pier pad size _____

Other information

_____
_____
_____
_____
_____
_____
